

# GLX Tufts Interlocking Early Works



31-May-17



**massDOT**  
Massachusetts Department of Transportation



# Agenda

## Medford GLX Project Neighborhood Meeting

*May 31, 2017; 6:30 PM – 7:30 PM*

1. **Welcome/Introductions** - Joe Nolan (City Point Partners)
2. **Early Works Construction Overview and Schedule** - Paul Hadley (MBTA) & Randy Henke (HNTB)
3. **Public Outreach & Contacting the Project** - Joe Nolan (City Point Partners)
4. **Upcoming Public Meetings**
5. **Q & A**




# Tufts Interlocking

Current Track Alignment Future Track Alignment

← COLLEGE AVE

← COLBY STREET →

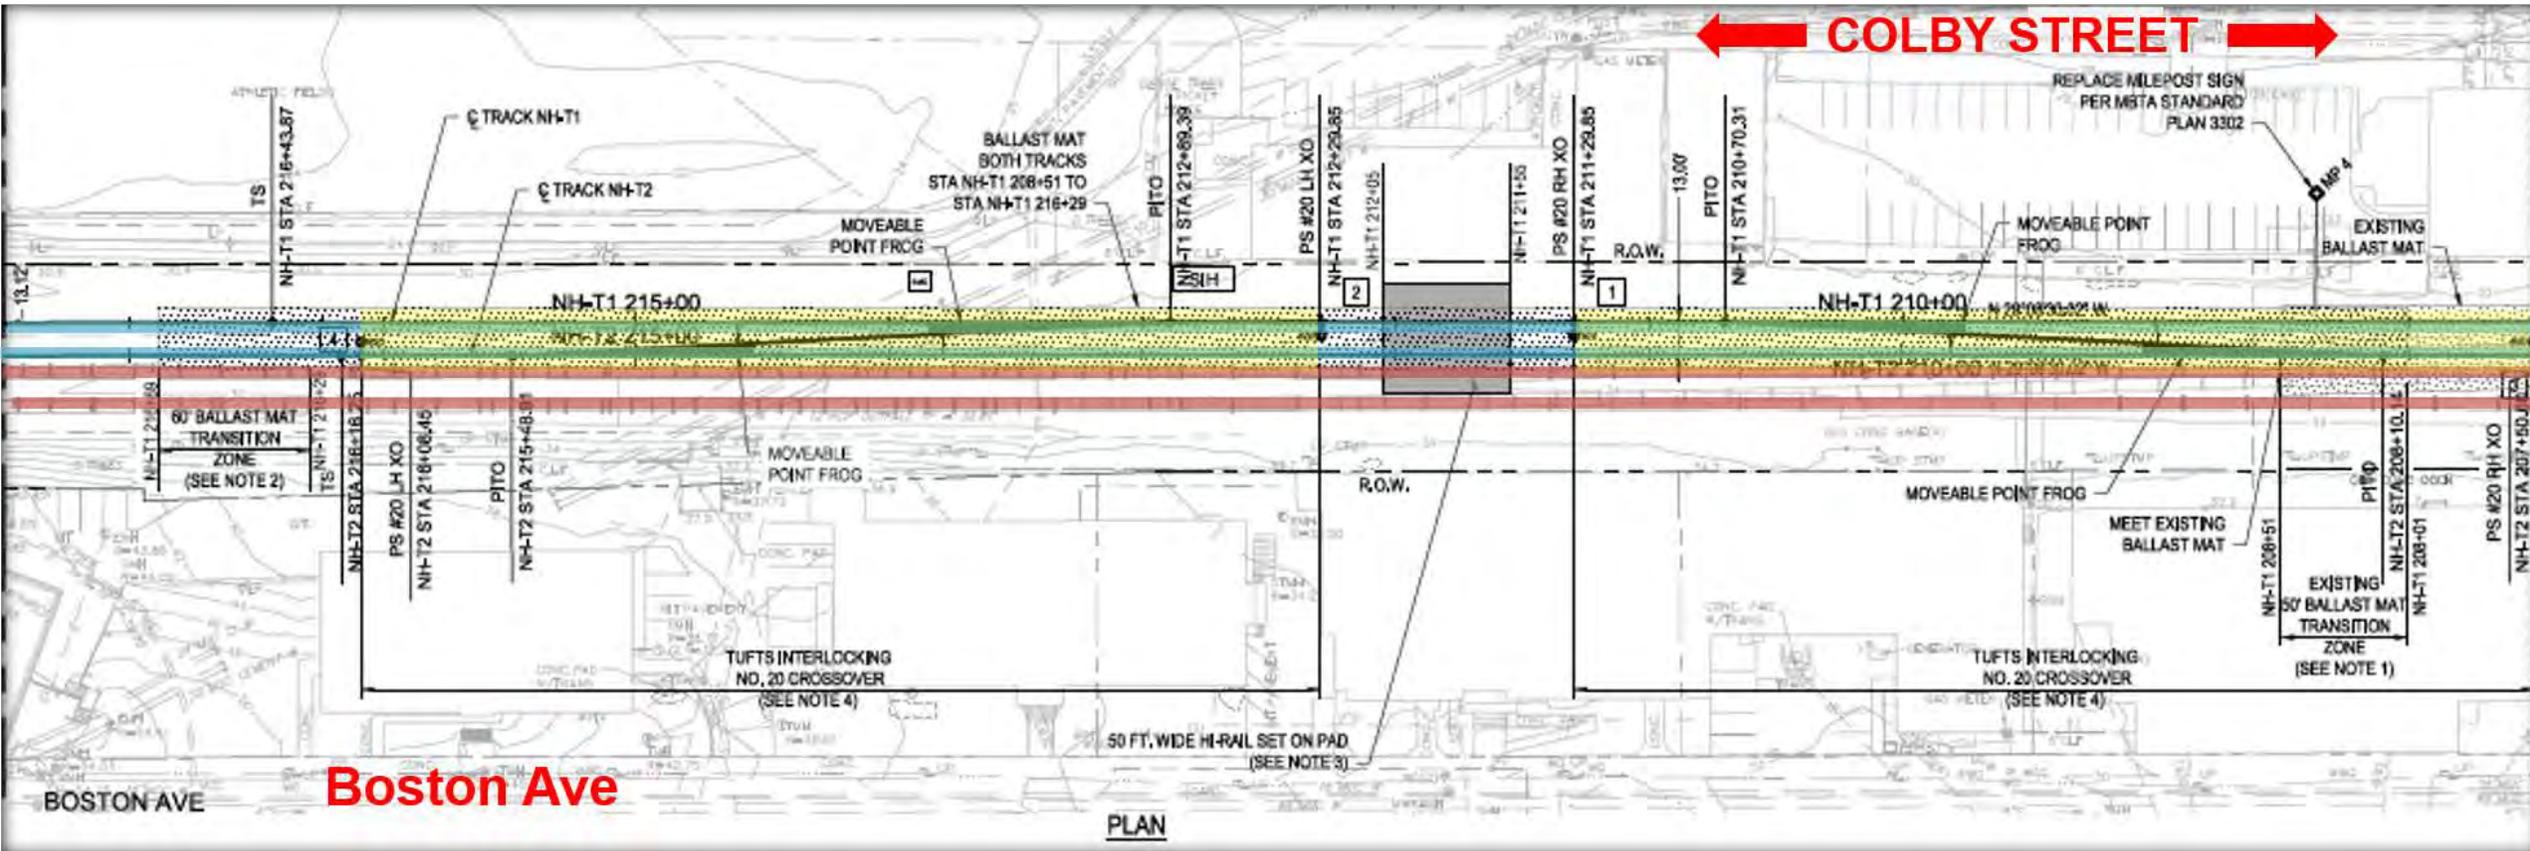

Boston Ave

HARVARD STREET →

PLAN




massDOT  
Massachusetts Department of Transportation



# Signal Location

Current Track Alignment Future Track Alignment

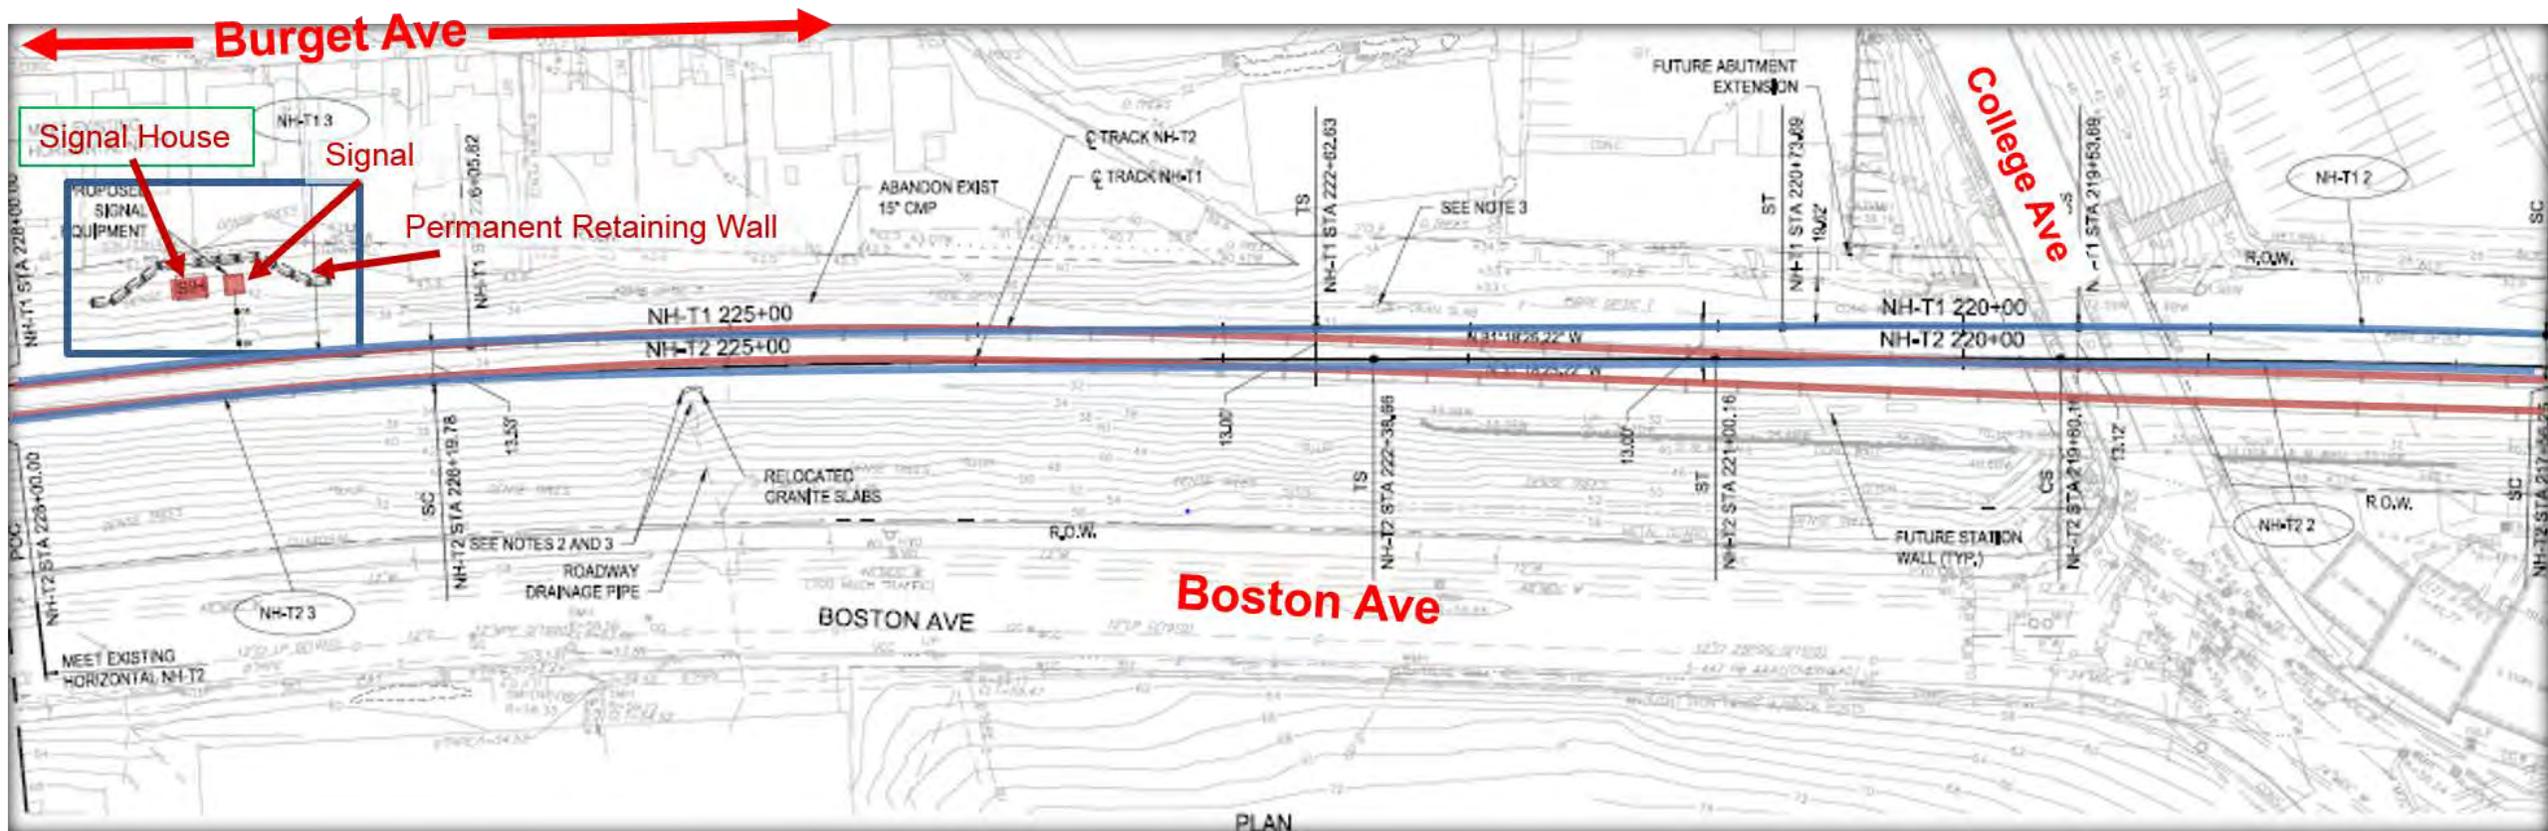


# Examples of Signal Equipment



Signal House & Signal



# Proposed Permanent Condition

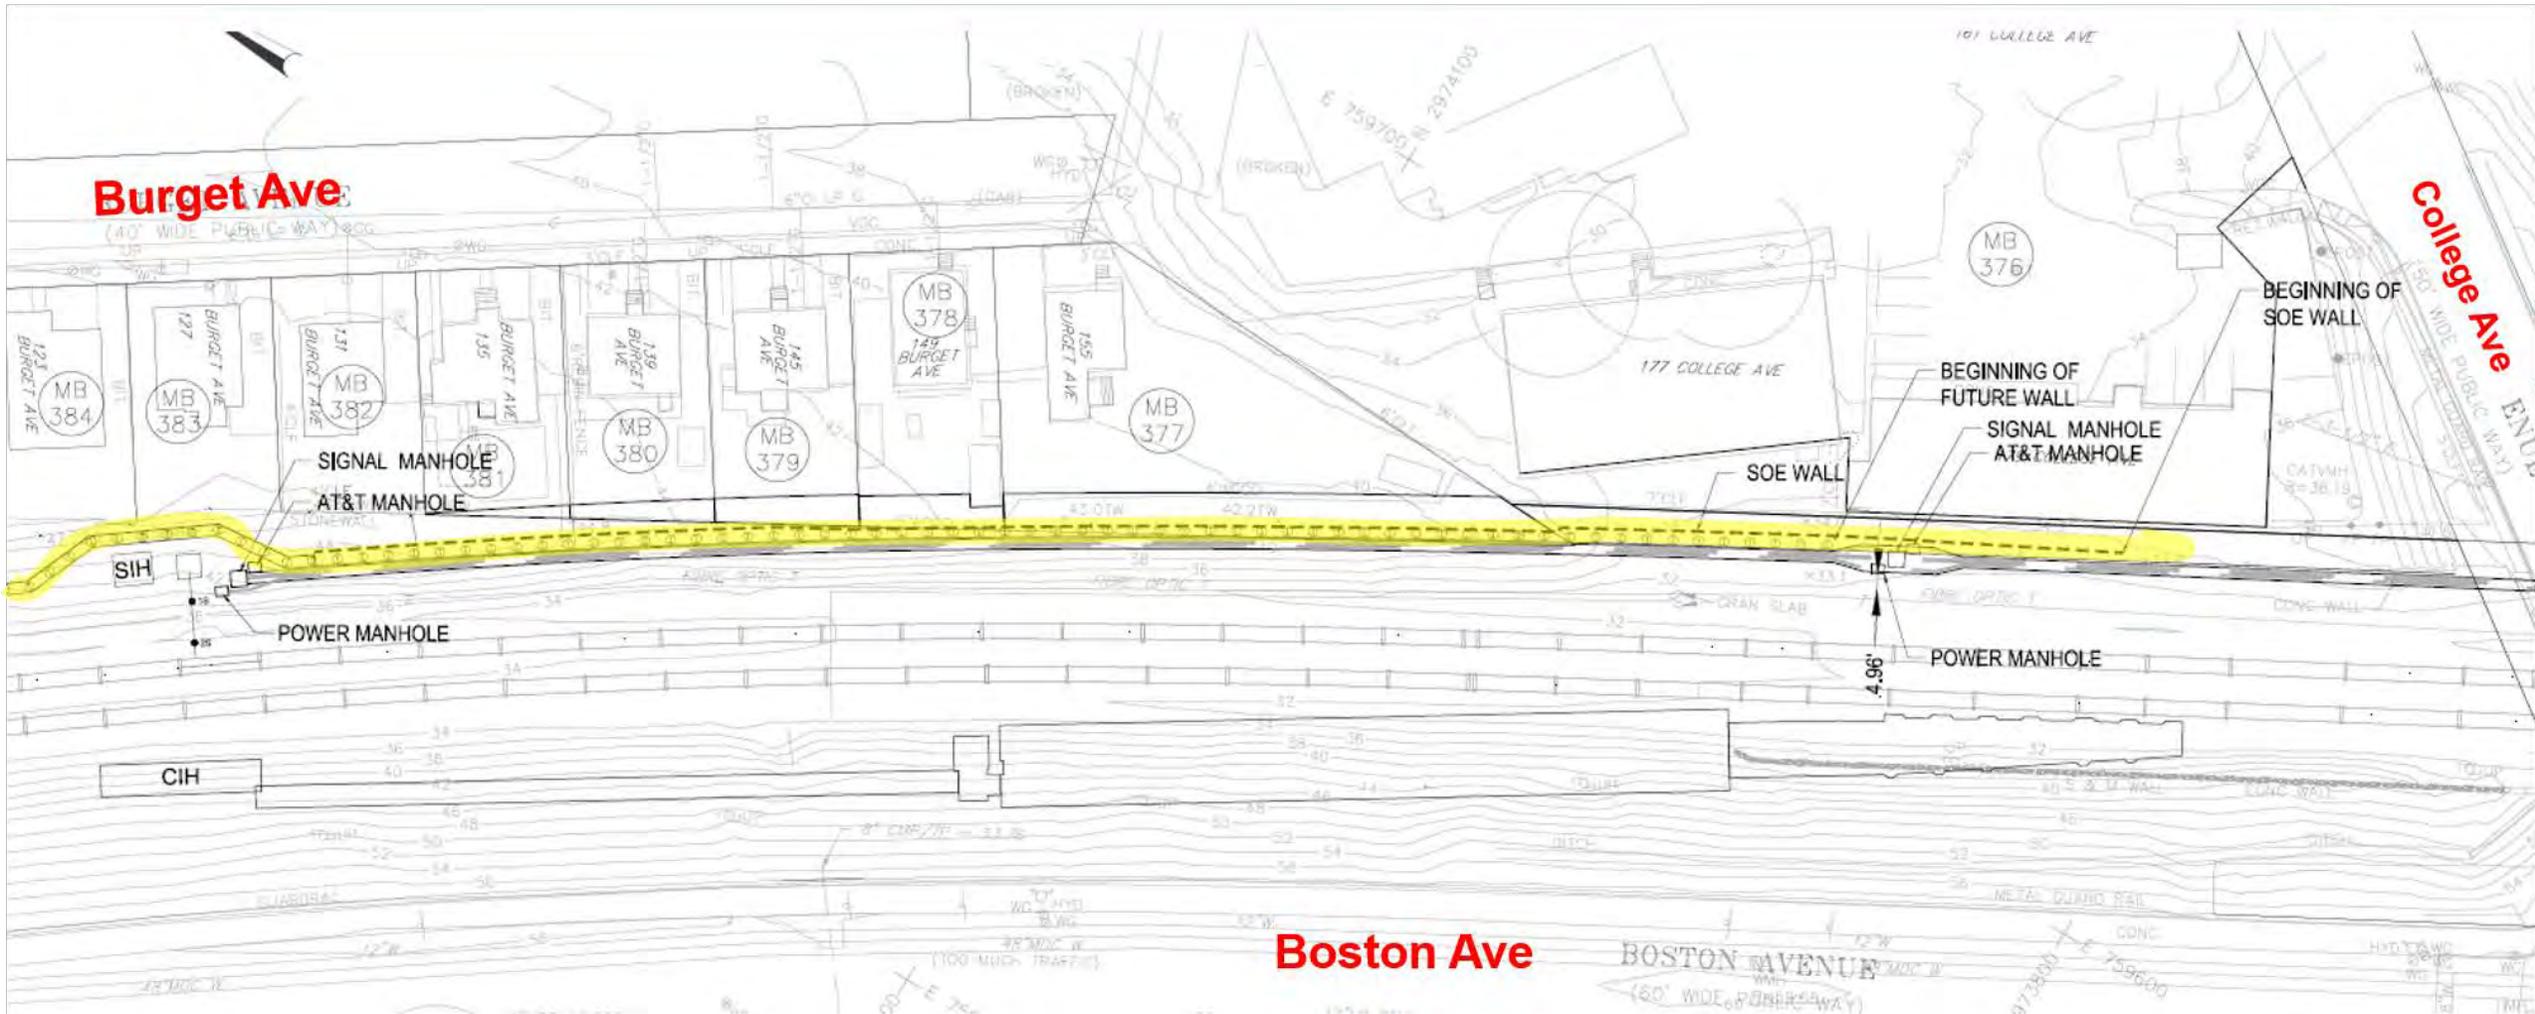


# Examples of Walls



# Construction Equipment & Materials Traffic

## Potential Routes

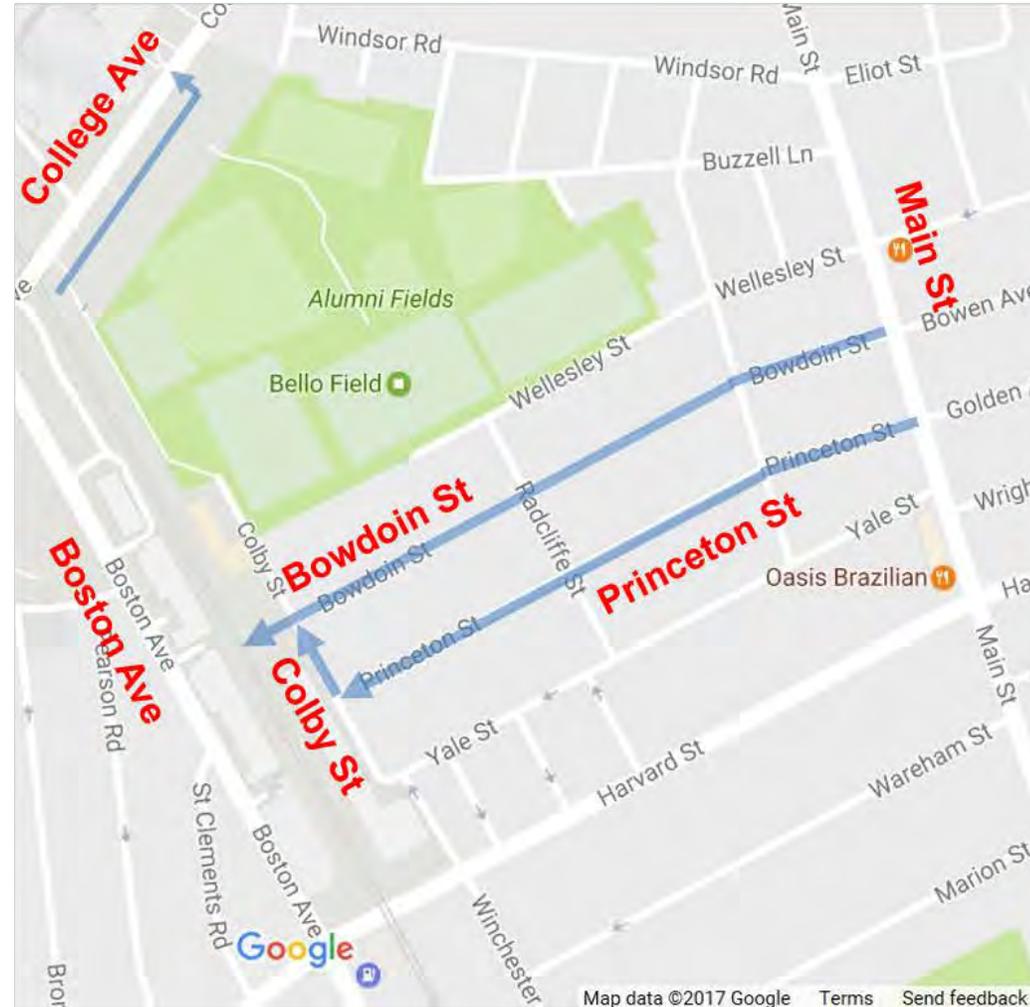

# Keolis Schedule\*

## Tufts Interlocking Schedule of Work for 2017

Generally construction activities will occur weekdays from approximately 7:00 AM to 5:30 PM

### Mobilize and Deliver Track Material

- Ongoing June 2017

### Site & Conduit Work

- Grading required for utilities and new alignment of Track #1, Ongoing to late May/early June 2017

### Installation of support of excavation, conduit and manholes

- June to August 2017

### Fine grading and install ballast mat for Track #2

- September 2017

### Construction of South Signal House and Retaining Wall

- Work begins August 2017 through the Fall and then to resume in the Spring (March 2018)

**\*Due to the nature of construction, schedules are subject to change**

# Design Build Schedule\*

## PROJECT SCHEDULE HIGHLIGHTS

1. Federal Transit Administration (FTA) Risk Refresh 1/25/17 -1/26/17 (Actual)
2. Issue Draft Request for Proposals for DB Shortlist 3/15/17 (Actual)
3. Hold One-on-Ones 3/28/17 – 5/10/17 (Actual)
4. Issue Final RFP 5/23/17 (Actual)
5. Alternative Technical Concept (ATC) Process 5/30/17 – 8/9/17
6. FTA Finance Plan Submission 5/31/17
7. Design Build Proposals Due 9/28/17
8. Bid Opening/Select Design Build Entity 11/28/17
9. Notice to Proceed to Design Build Entity 2/9/18
10. Project Completion 12/10/21

**\*Due to the nature of construction, schedules are subject to change**



# Public Outreach During Early Works Construction

- Contact the project
  - GLX Email: [info@glxinfo.com](mailto:info@glxinfo.com)
  - GLX Hotline: 1-855-GLX-INFO (24/7 coverage)
- Email blasts and GLX website updates (ongoing)
- Neighborhood database
  - Sign-up with contact info at this meeting
  - Targeted neighborhood updates



# Upcoming Meetings

## **GLX Medford Public Meeting**

June 21, 2017 6:00 to 7:30 PM

Medford City Hall Council Chambers

85 George P Hassett Dr, Medford, MA

## **GLX Somerville Public Meeting**

***Date To Be Determined***

Somerville High School Auditorium

81 Highland Ave, Somerville, MA



# Medford GLX Project Neighborhood Meeting

**Questions/Comments?**

